



PREFABRICATED OFFICE CABINS

Technical specification, approved GA and price guide - six controlled sizes



Six approved prefabricated office cabin options

Prices below are copied from prefabricated-office-cabins-technical-specification-and-price-dashboard.xlsx.

Size	Area	Rate / sq ft	Price ex GST	Price incl GST	Approved option	Roof
10 x 10 ft	100 sq ft	INR 1,495	INR 149,500	INR 176,410	10-COMPACT-10-STANDARD	Two-way 5-6 in rise
20 x 8 ft	160 sq ft	INR 1,430	INR 228,800	INR 269,984	20-OPEN-08	One-way 5-6 in fall
20 x 10 ft	200 sq ft	INR 1,300	INR 260,000	INR 306,800	20-MANAGER-TEAM-10-SNC-V1	Two-way 5-6 in rise
20 x 12 ft	240 sq ft	INR 1,248	INR 299,520	INR 353,434	20-MANAGER-TEAM-12-SNC-V1	Two-way 5-6 in rise
30 x 10 ft	300 sq ft	INR 1,248	INR 374,400	INR 441,792	30-OPEN-10-MAXIMUM	Two-way 5-6 in rise
40 x 10 ft	400 sq ft	INR 1,235	INR 494,000	INR 582,920	40-TWIN-MANAGER-COMMON-10-SNC-V1	Two-way 5-6 in rise

Commercial boundaries

- Final quotation, delivery, foundations/supports, transport, unloading, installation, taxes and project-specific services govern supply.
- Furniture shown in presentation images is illustrative and excluded unless specifically included in the signed quotation.
- Prices and GA are buyer guidance, not structural calculations or fabrication instructions.

Porta-cabin material family

Bottom frame

100 x 50 x 3 mm MS C-channel baseline

Floor support

MS base/cross-member grid with 18 mm Bison/cement-fibre board

Top frame

50 x 50 x 1.6 mm MS square pipe baseline

Roof frame

50 x 50 x 1.2 mm primary members with approved secondary members

Posts / walls

50 x 50 x 2 mm square pipe or approved 60 x 60 mm angles

Exterior wall

1.2 mm specially corrugated MS sheet

Roof sheet

1.4 mm corrugated MS sheet

Interior / ceiling

8 mm pre-laminated MDF with aluminium joints

Floor finish

18 mm Bison board with 1.3 mm vinyl

Wall insulation

25 mm glass wool or 12 mm Heatlon, as quoted

Roof insulation

50 mm glass wool, nominal 42 kg/m3

External door

7 x 3 ft outward-opening MS-framed door baseline

Windows

Two-track powder-coated aluminium with 4 mm glass

Electrical starts

1.5 sq.mm lighting; 2.5 sockets; 4 higher-load/AC

These sections and materials are baseline specification references, not universal structural verification.

Final loads, spans, supports, lifting, wind, seismic, openings, insulation/finish choices and signed quotation govern.

TECHNICAL DIAGRAM 1 - FRAME AND SHEET JOINT



FRAME AND CORRUGATED-SHEET JOINT

Buyer-facing construction sequence - illustrative, not a fabrication detail


1 PREPARE AND ALIGN



Check square and diagonals


- Cut and deburr members
- Square, clamp and dimension-check
- Verify diagonals before joining

2 TACK, VERIFY, WELD

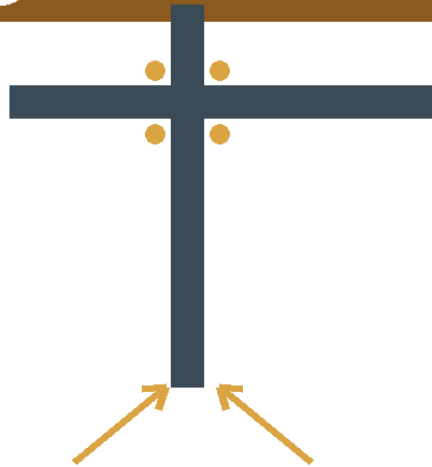

- Use opposed tacks to control pull
- Recheck level, square and diagonals
- Complete weld to qualified procedure

3 PRIME, SEAL, FIX SHEET

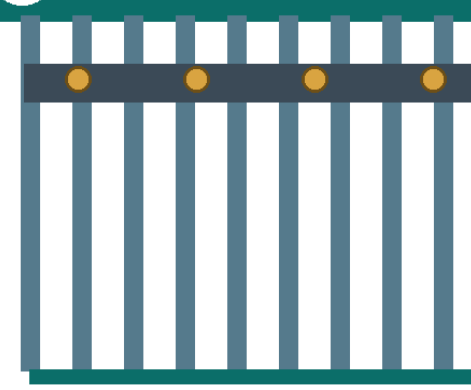

EPDM/butyl washer + compatible seal

- Clean joint and repair coating
- Align corrugations and closures
- Seal weather line; inspect final fixing

ENGINEERING BOUNDARY

Approved shop drawings, project engineering, qualified welding procedures, coating system and project QA govern final member selection, joints, fasteners and weathering.



WINDOW, ELECTRICAL AND FAN INSTALLATION

Protected openings and circuits - final load schedule and licensed work govern


1 SET AND SEAL WINDOW



Level - plumb - square - flash - seal

- Reinforce opening and anchor frame
- Provide flashing and perimeter seal
- Inspect drainage and weather line


2 DISTRIBUTE CIRCUITS

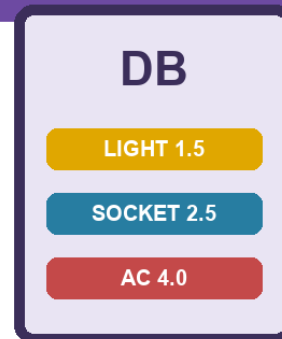

Isolation + RCCB/MCB + earthing

- Segregate lighting, socket and AC
- Provide isolation, protection and earth
- Cable sizes are starting values only

3 INSTALL AND TEST



Fan, light, socket, data/UPS and AC

- Test continuity and insulation
- Check polarity, earthing and RCCB trip
- Commission only to final schedule

ENGINEERING BOUNDARY


Final load schedule, cable derating, voltage drop, fault level, protection, equipment selection, earthing and licensed electrical work govern the completed installation.

SAMAN PREFABRICATED OFFICE CABINS

DETAILED GA & WEBSITE ASSET CONTROL BOARD — 10 x 10 x 8.5 ft

USER-APPROVED GA / V1

DIMENSIONED PLAN & WALL IDENTITY — 10-COMPACT-10-STANDARD

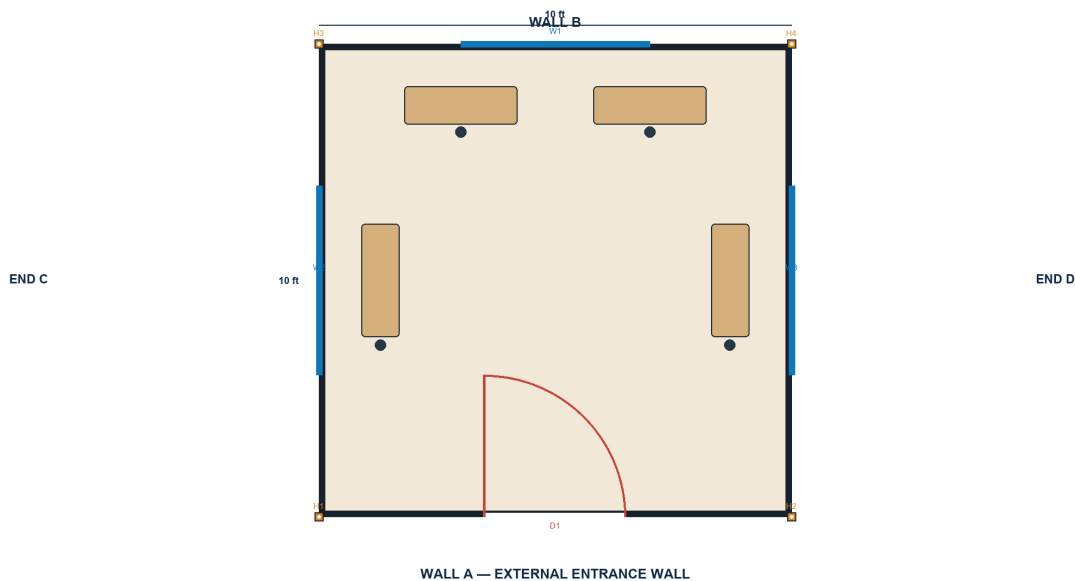


LOCKED OPENING / USE SCHEDULE


- Option: 10-COMPACT-10-STANDARD — USER-APPROVED-GA
- Size: 10 x 10 x 8.5 ft (100 sq.ft.)
- Use: Compact four-workstation office
- Openings: 1 external door(s); 3 windows
- Roof: Marginal two-way, 5-6 in ridge rise
- Lifting: H1-H4, exactly four compact top-corner eye plates
- Furniture: 4 workstations | 1 external door | 3 windows
- Price: Rs 1,49,500 ex GST; Rs 1,76,410 incl 18% GST

ROOF ORIENTATION + HOOK LOCK


FULL-LENGTH CENTRED RIDGE — ONLY 5-6 IN ABOVE EAVES




WALL A ELEVATION

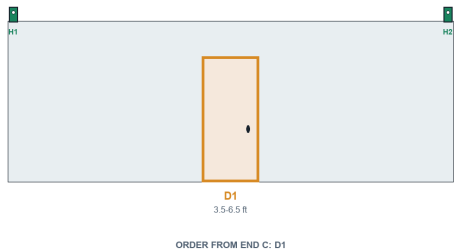


WALL B ELEVATION

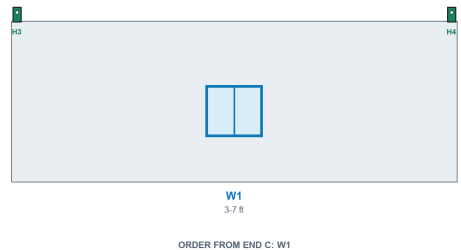

END C ELEVATION

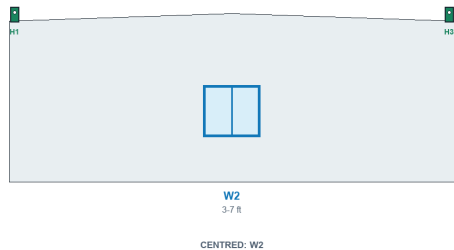

END D ELEVATION

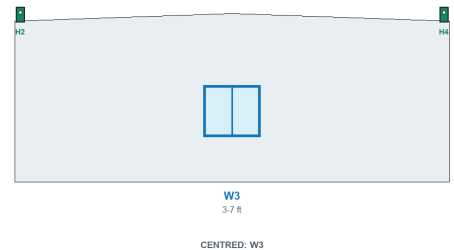


SAMAN PREFABRICATED OFFICE CABINS

DETAILED GA & WEBSITE ASSET CONTROL BOARD — 20 x 8 x 8.5 ft

USER-APPROVED GA / V1

DIMENSIONED PLAN & WALL IDENTITY — 20-OPEN-08

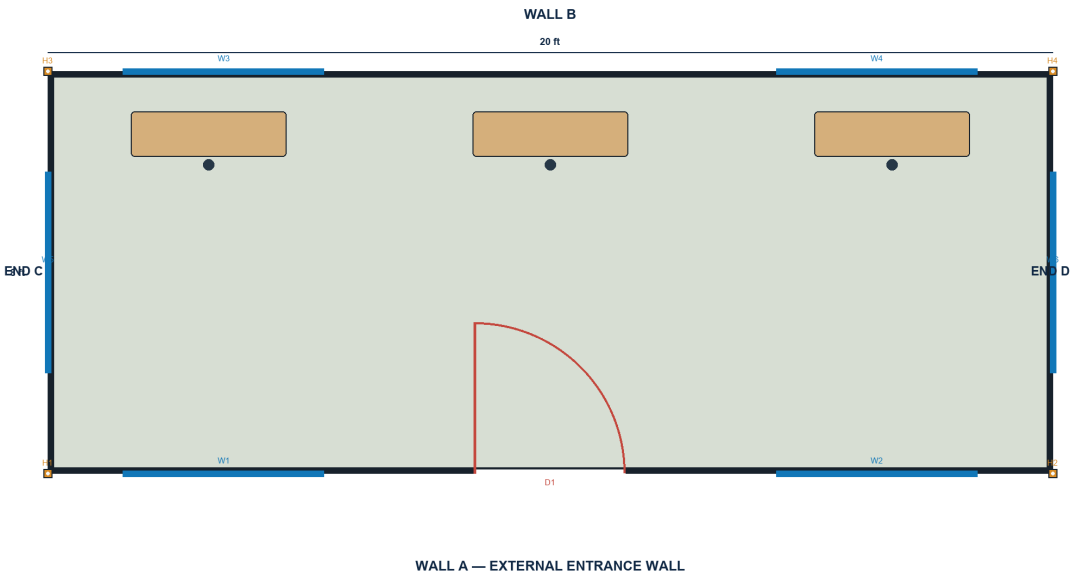

LOCKED OPENING / USE SCHEDULE


- Option: 20-OPEN-08 — USER-APPROVED-GA
- Size: 20 x 8 x 8.5 ft (160 sq.ft.)
- Use: Open office - three workstations
- Openings: 1 external door(s); 6 windows
- Roof: Marginal one-way, 5-6 in total fall
- Lifting: H1-H4, exactly four compact top-corner eye plates
- Furniture: 3 workstations | 1 external door | 6 windows
- Price: Rs 2,28,800 ex GST; Rs 2,69,984 incl 18% GST

ROOF ORIENTATION + HOOK LOCK

ONE PLANE ACROSS WIDTH — TOTAL FALL ONLY 5-6 IN




WALL A ELEVATION




WALL B ELEVATION



END C ELEVATION



END D ELEVATION




SAMAN PREFABRICATED OFFICE CABINS

DETAILED GA & WEBSITE ASSET CONTROL BOARD — 20 x 10 x 8.5 ft

USER-APPROVED GA / V1

DIMENSIONED PLAN & WALL IDENTITY — 20-MANAGER-TEAM-10-SNC-V1

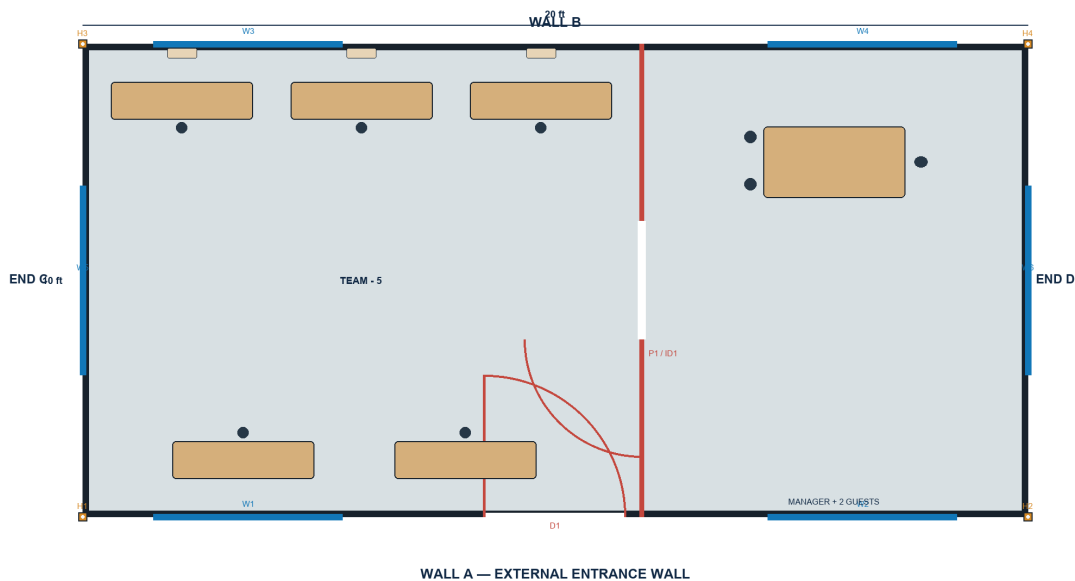


LOCKED OPENING / USE SCHEDULE


- Option: 20-MANAGER-TEAM-10-SNC-V1 — USER-APPROVED-GA
- Size: 20 x 10 x 8.5 ft (200 sq.ft.)
- Use: Manager room + five-person team office
- Openings: 1 external door(s); 6 windows
- Roof: Marginal two-way, 5-6 in ridge rise
- Lifting: H1-H4, exactly four compact top-corner eye plates
- Furniture: 5 team workstations | manager + 2 guests | 1 partition
- Price: Rs 2,60,000 ex GST; Rs 3,06,800 incl 18% GST
- Partition: P1 at 11 ft 10 in; ID1 centred on the clear aisle

ROOF ORIENTATION + HOOK LOCK

FULL-LENGTH CENTRED RIDGE — ONLY 5-6 IN ABOVE EAVES




WALL A ELEVATION

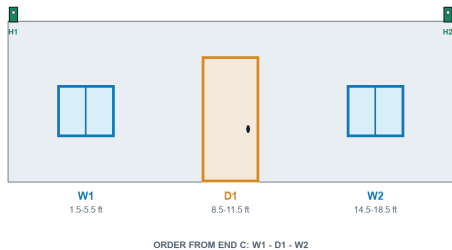


WALL B ELEVATION



END C ELEVATION

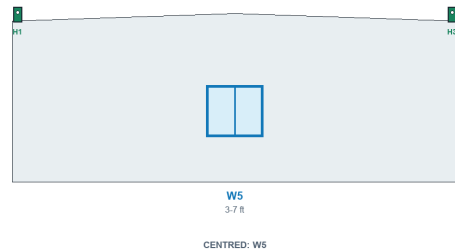

END D ELEVATION

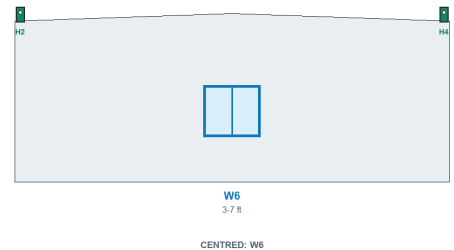


SAMAN PREFABRICATED OFFICE CABINS

DETAILED GA & WEBSITE ASSET CONTROL BOARD — 20 x 12 x 8.5 ft

USER-APPROVED GA / V1

DIMENSIONED PLAN & WALL IDENTITY — 20-MANAGER-TEAM-12-SNC-V1

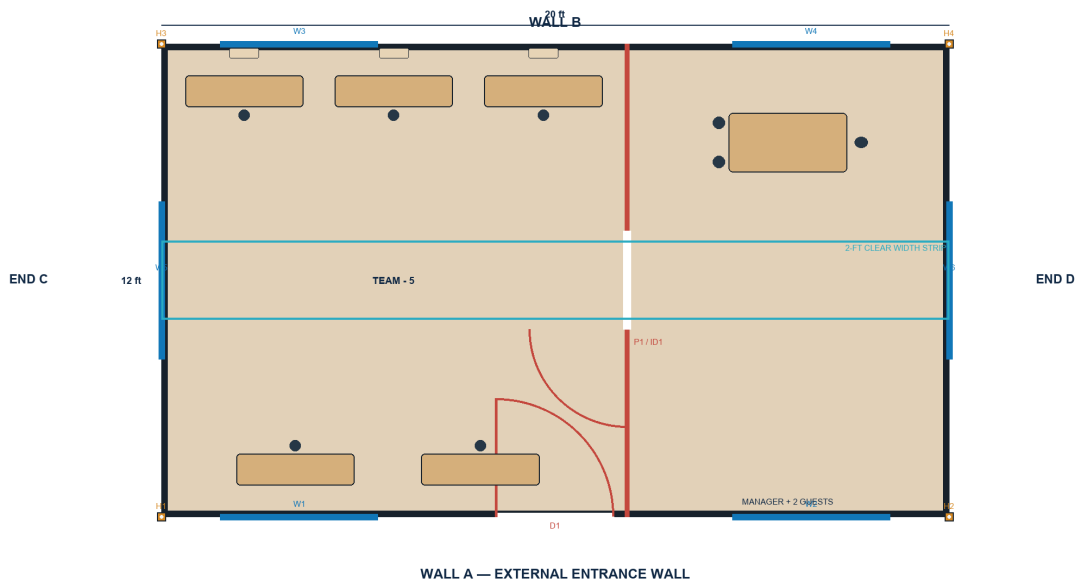


LOCKED OPENING / USE SCHEDULE


- Option: 20-MANAGER-TEAM-12-SNC-V1 — USER-APPROVED-GA
- Size: 20 x 12 x 8.5 ft (240 sq.ft.)
- Use: Widened manager/team office; 2-ft clear strip
- Openings: 1 external door(s); 6 windows
- Roof: Marginal two-way, 5-6 in ridge rise
- Lifting: H1-H4, exactly four compact top-corner eye plates
- Furniture: Same longitudinal ledger as 20x10 | 2-ft wider
- Price: Rs 2,99,520 ex GST; Rs 3,53,434 incl 18% GST
- Derivative lock: same 20x10 longitudinal ledger + continuous 2-ft clear strip
- Partition: P1 at 11 ft 10 in; ID1 centred on the clear aisle

ROOF ORIENTATION + HOOK LOCK


FULL-LENGTH CENTRED RIDGE — ONLY 5-6 IN ABOVE EAVES




WALL A ELEVATION

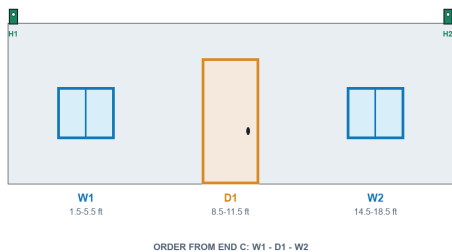


WALL B ELEVATION

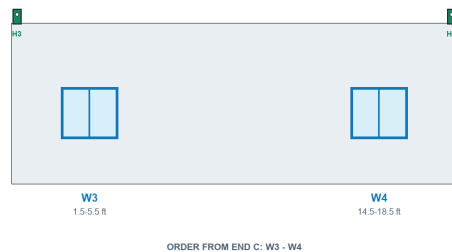

END C ELEVATION

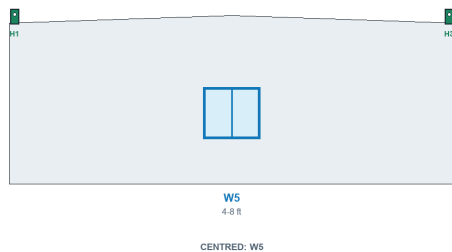

END D ELEVATION

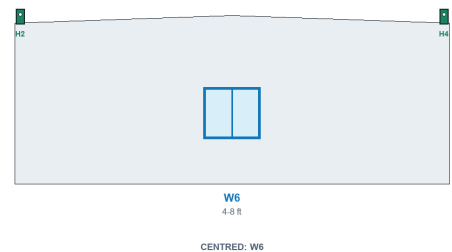


SAMAN PREFABRICATED OFFICE CABINS

DETAILED GA & WEBSITE ASSET CONTROL BOARD — 30 x 10 x 8.5 ft

USER-APPROVED GA / V1

DIMENSIONED PLAN & WALL IDENTITY — 30-OPEN-10-MAXIMUM

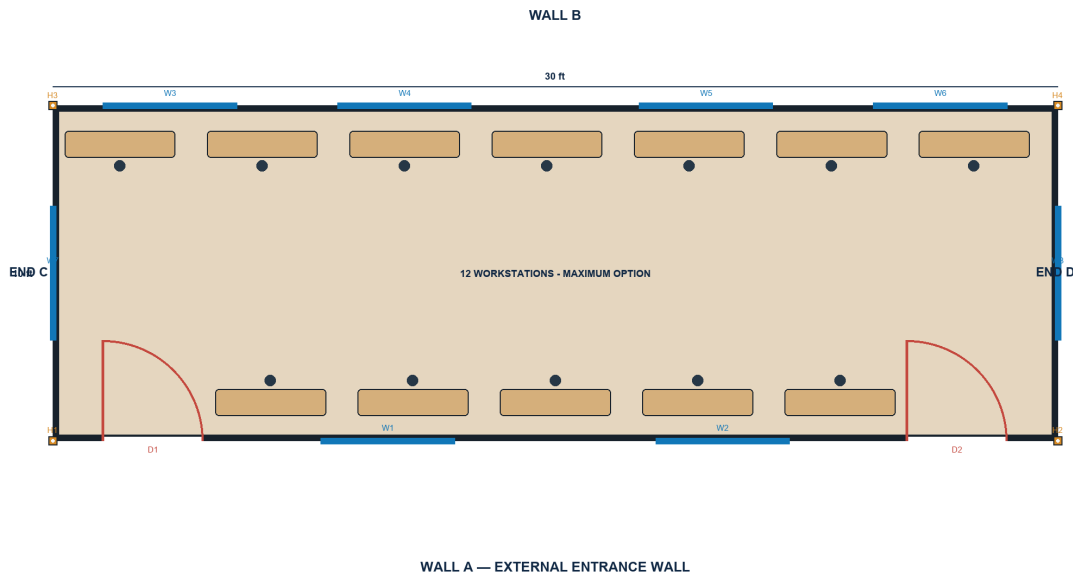


LOCKED OPENING / USE SCHEDULE

- Option: 30-OPEN-10-MAXIMUM — USER-APPROVED-GA
- Size: 30 x 10 x 8.5 ft (300 sq.ft.)
- Use: Maximum-capacity open office
- Openings: 2 external door(s); 8 windows
- Roof: Marginal two-way, 5-6 in ridge rise
- Lifting: H1-H4, exactly four compact top-corner eye plates
- Furniture: 12 workstations: 5 Wall A + 7 Wall B | 2 doors
- Price: Rs 3,74,400 ex GST; Rs 4,41,792 incl 18% GST

ROOF ORIENTATION + HOOK LOCK

FULL-LENGTH CENTRED RIDGE — ONLY 5-6 IN ABOVE EAVES




WALL A ELEVATION




ORDER FROM END C: D1 - W1 - W2 - D2

WALL B ELEVATION




ORDER FROM END C: W3 - W4 - W5 - W6

END C ELEVATION



CENTRED: W7

END D ELEVATION



CENTRED: W8


APPROVED GA BOARD - 40 x 10 FT

SAMAN PREFABRICATED OFFICE CABINS

DETAILED GA & WEBSITE ASSET CONTROL BOARD — 40 x 10 x 8.5 ft

USER-APPROVED GA / V1

DIMENSIONED PLAN & WALL IDENTITY — 40-TWIN-MANAGER-COMMON-10-SNC-V1

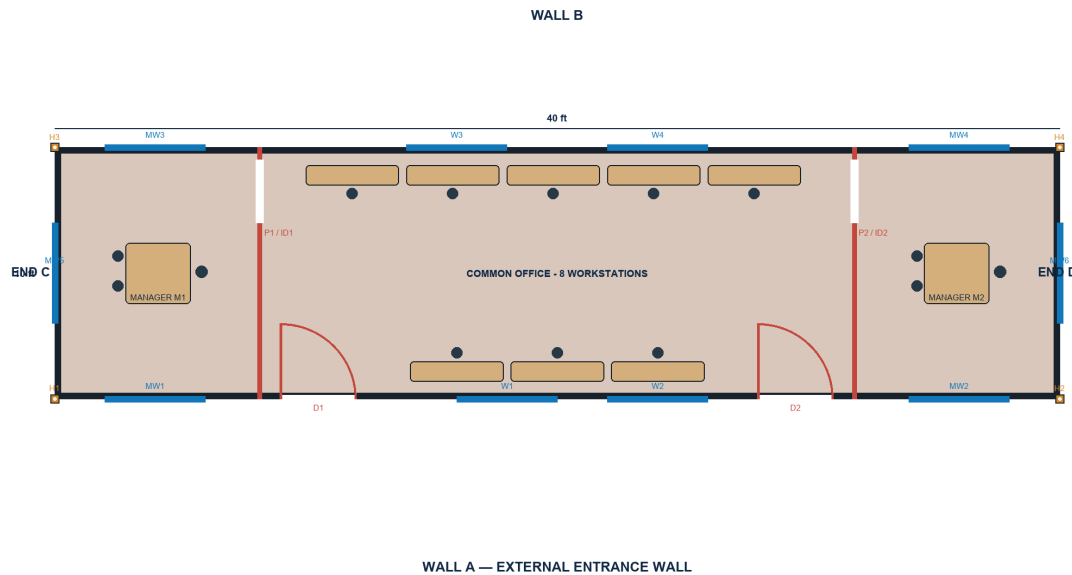

LOCKED OPENING / USE SCHEDULE

- Option: 40-TWIN-MANAGER-COMMON-10-SNC-V1 — USER-APPROVED-GA
- Size: 40 x 10 x 8.5 ft (400 sq.ft.)
- Use: Twin manager rooms + eight-person common office
- Openings: 2 external door(s); 10 windows
- Roof: Marginal two-way, 5-6 in ridge rise
- Lifting: H1-H4, exactly four compact top-corner eye plates
- Furniture: 8 common workstations | 2 managers + 4 guests | 2 partitions
- Price: Rs 4,94,000 ex GST; Rs 5,82,920 incl 18% GST
- Partitions: P1 at 8 ft 2 in; P2 at 31 ft 10 in; ID1 and ID2 near Wall A

ROOF ORIENTATION + HOOK LOCK


FULL-LENGTH CENTRED RIDGE — ONLY 5-6 IN ABOVE EAVES




WALL A ELEVATION




WALL B ELEVATION

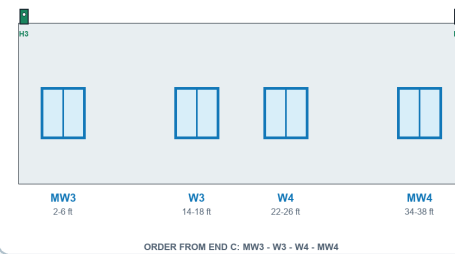

END C ELEVATION

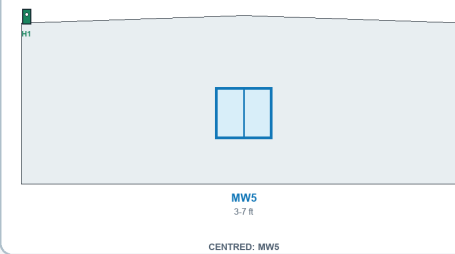

END D ELEVATION

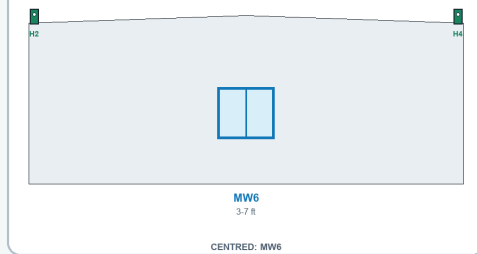

What the buyer should confirm before order

GA AND USE

- Confirm exact option ID, room use, furniture scope and opening coordinates.
- Exterior and interior openings must remain at identical physical coordinates.

ROOF AND DRAINAGE

- 8-ft width uses one-way marginal fall; 10/12-ft width uses a full-length centered ridge.
- The approved visual drainage rise/fall is only 5-6 inches; final detailing is project-engineered.

STRUCTURE AND LIFTING

- Exactly four compact top-corner lifting eye plates are shown; capacity and connections are not claimed.
- Approved shop drawings, signed calculations and project loading govern final members and lifting method.

ELECTRICAL AND SERVICES

- Final load schedule, protection, earthing, voltage drop, derating and licensed work govern.
- AC, data/UPS, fire systems and equipment are included only when stated in the signed quotation.

COMMERCIAL

- Furniture shown in images is presentation-only unless quoted.
- Transport, unloading, supports/foundation, installation, taxes and site work must be confirmed.

NOT FOR FABRICATION - CURRENT USER-APPROVED GA CONTROLS GEOMETRY

Final project engineering, approved shop drawings and signed quotation govern.
